Milestone Schedule

Project: Lenna Quarry
Job No.:
Date: April 15, 2004

DESILVA GATES CONSTRUCTION
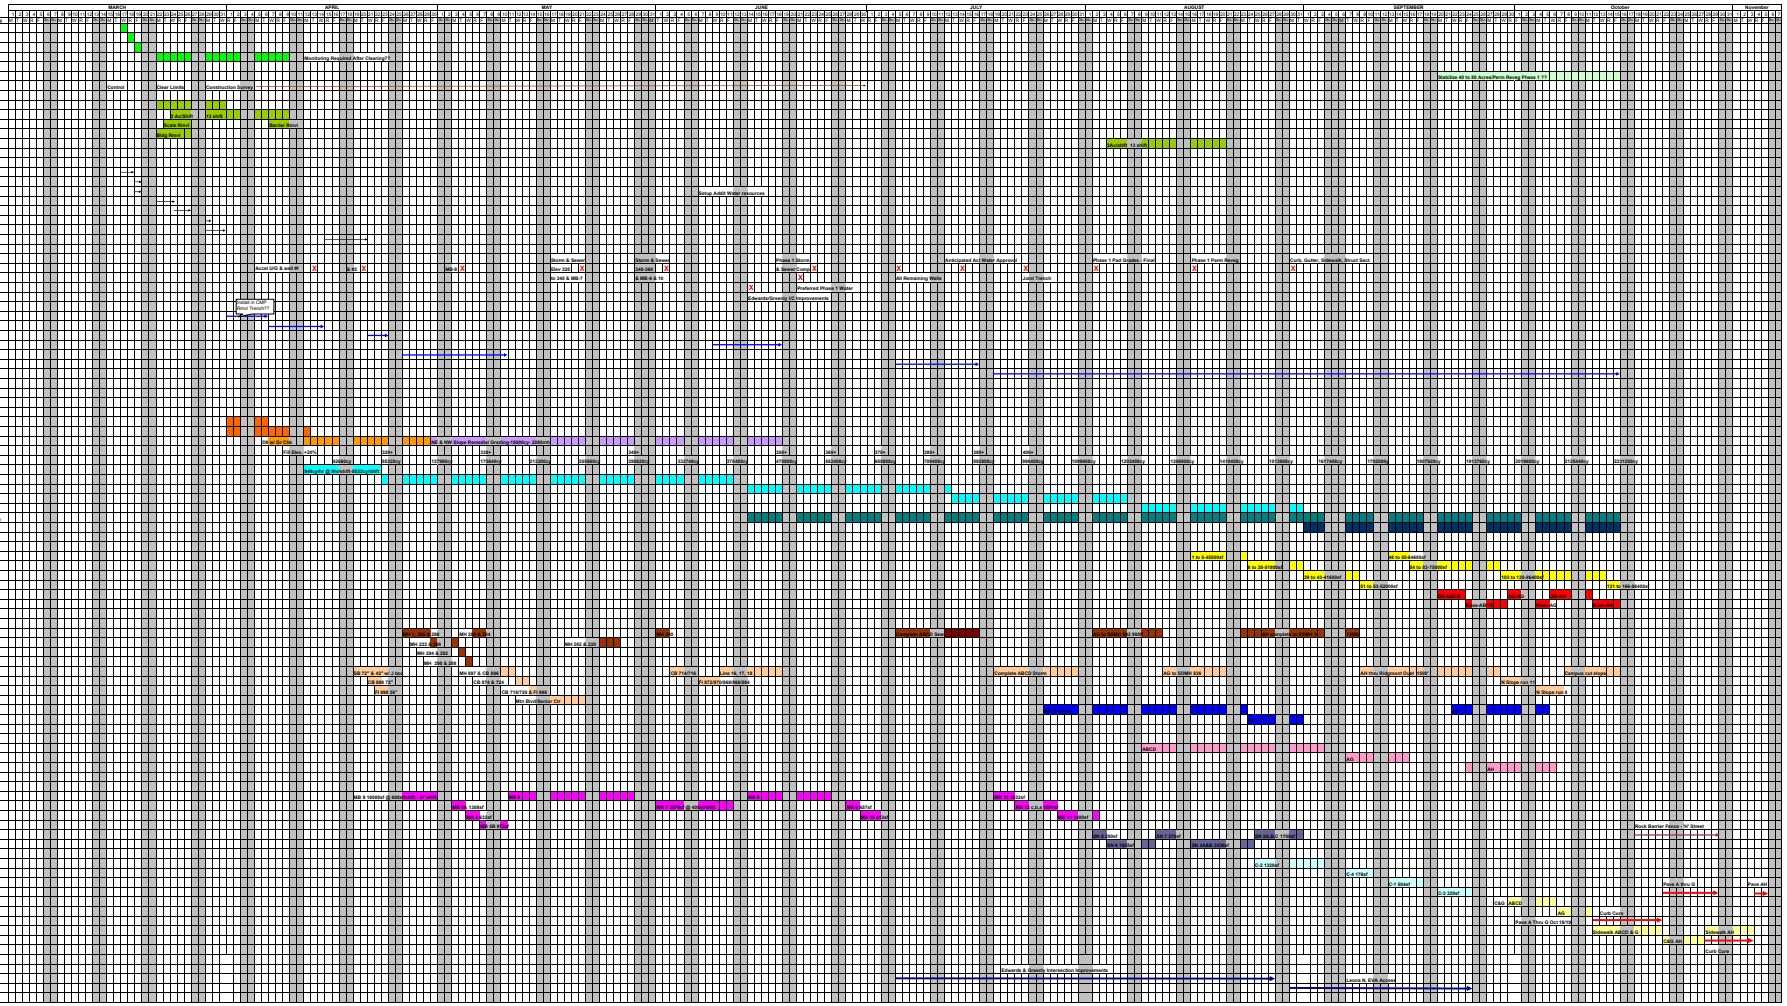
Location	Description of Work	Quantity
	Redlands Research Assoc-AWS Survey	1-day
	AWA-Breeding Bird/Raptor Survey	1-day
	AWA-Bat Roost Survey	1-day
	AWA-Monitoring	5-days
	Erosion Control Activities	
	Survey	
	Clearing Sub-Tree Removal	
	Clearing Sub-C & G Lower 40 Acre	
	Clearing Sub-Scale & Barrier Removal	
	Clearing Sub-Building Removal	
	Clearing Sub-C & G Upper 40 Acre	
	DSC-Miscellaneous Activities	
	Utility Locate	
	Water Setup-1 Main Tank Phase 1	
	Pothole/Disconnect Utilities	
	Install Silt Fence	3140lf
	Install Hay Fence	2000lf
	Tree Fencing	5000lf
	Remove Exig CMP	1000lf
	Site Prep/Office Setup	
	Approvals Req'd	
	Subdrain	
	Cond Discharge Pipe-Lower Fill	1000lf
	Subdrain-Lower Fill Det Basin	3000lf
	Area A	1000lf
	Area B & C	3000lf
	Streets C & H	4000lf
	Area D	3000lf
	Upper Bowl & Ridge	27,000lf
	Excavation	
	Fill Prep Lower Area	375,000cy
	Detention Basin Exc. Q could be tie 8000cy from c	112,75cy
	Pioneering to Upper Ridge	21,000
	SIP's	
	Area A	70,447cy
	Area B	59,915cy
	Area D	178,633cy
	Area E	158,000cy
	Area F	144,575cy
	Center Ridge Cut & H Street	580,195cy
	Upper Slope Cut	88,657cy
	Street & Lot Undercut	105,000cy
	Finish-Pads	
	Finish-Streets	
	Pipe/Ut Trench	
	Sewer @ 135 lf/shift	
	Storm @ 150 lf/shift	
	Water @ 150 lf/shift	
	U Trench @ 150 lf/shift	
	Walls	
	Conc Block	
	Soil Nail Wall	
	CIP Wall	
	Asphalt Paving - Curb/Gutter/Sidewalk	
	Off Site Improvements
